



ID	Task Mode	Unique ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	23	Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025	
									Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
1		1	Bid Letting	0 days	Wed 10/18/23	Wed 10/18/23																							
2		2	Contracts Turned Around	30 days	Wed 10/18/23	Tue 11/28/23	1																						
3		3	Precon	0 days	Mon 12/18/23	Mon 12/18/23																							
4		4	Stage 0 - WL Improvements {5th to Main}	49 days	Tue 1/2/24	Fri 3/8/24																							
5		5	Clearing and Grubbing/Tree Removal	9 days	Tue 1/2/24	Fri 1/12/24	3FS+5 days																						
6		6	Every Removals	4 days	Thu 1/11/24	Tue 1/16/24																							
7		114	Pothole gas services (Kinetic Energy)	2 days	Tue 1/16/24	Wed 1/17/24																							
8		111	Sidewalk removals for water line	3 days	Wed 1/17/24	Fri 1/19/24																							
9		112	Traffic Control (NB ONLY)	1 day	Mon 1/22/24	Mon 1/22/24	8																						
10		7	Waterline Improvements	35 days	Mon 1/22/24	Fri 3/8/24	8																						
11		8	Stage 1 - 5th to Main {EASTSIDE IMPRV}	59 days	Mon 3/11/24	Thu 5/30/24																							
12		9	Set Traffic Control (NB ONLY)	1 day	Mon 3/11/24	Mon 3/11/24	10																						
13		10	Clearing and Grubbing	1 day	Tue 3/12/24	Tue 3/12/24	12																						
14		11	Rock Ex	3 days	Wed 3/13/24	Fri 3/15/24	13																						
15		12	Drainage Improvements	20 days	Mon 3/18/24	Fri 4/12/24	14																						
16		13	Common Ex	5 days	Thu 4/4/24	Wed 4/10/24	15FS-7 days																						
17		14	Finegrade	2 days	Thu 4/11/24	Fri 4/12/24	16																						
18		15	Crushed Rock Base	5 days	Mon 4/15/24	Fri 4/19/24	17																						
19		16	PCCP Mainline	10 days	Fri 4/19/24	Thu 5/2/24	18FS-1 day																						
20		20	Electrical Improvements	5 days	Fri 5/3/24	Thu 5/9/24	19																						
21		17	C&G Slips/Handpours/Hookups	3 days	Fri 5/3/24	Tue 5/7/24	19																						
22		18	Drives & Valley Gutters	10 days	Wed 5/8/24	Tue 5/21/24	21																						
23		19	Sidewalk, WCRs and Misc.	5 days	Wed 5/22/24	Tue 5/28/24	22																						
24		21	Seeding/Eros Control	2 days	Wed 5/29/24	Thu 5/30/24	23																						
25		22	Stage 2 - 5th to Main {WESTSIDE IMPRV}	47 days	Fri 5/31/24	Mon 8/5/24																							
26		23	Set Traffic Control (NB ONLY)	1 day	Fri 5/31/24	Fri 5/31/24	24																						
27		24	Clearing and Grubbing	1 day	Mon 6/3/24	Mon 6/3/24	26																						
28		25	Rock Ex	3 days	Tue 6/4/24	Thu 6/6/24	27																						
30		27	Common Ex	5 days	Thu 6/6/24	Wed 6/12/24	27FS+2 days																						
29		26	Drainage Improvements	6 days	Fri 6/7/24	Fri 6/14/24	28																						
31		28	Finegrade	2 days	Thu 6/13/24	Fri 6/14/24	30																						
32		29	Crushed Rock Base	5 days	Mon 6/17/24	Fri 6/21/24	31																						
33		30	PCCP Mainline	8 days	Fri 6/21/24	Tue 7/2/24	32FS-1 day																						
34		34	Electrical Improvements	5 days	Wed 7/3/24	Tue 7/9/24	33																						
35		31	C&G Slips/Handpours/Hookups	5 days	Wed 7/3/24	Tue 7/9/24	33																						
36		32	Drives & Valley Gutters	10 days	Wed 7/10/24	Tue 7/23/24	35																						
37		33	Sidewalk, WCRs and Misc.	5 days	Wed 7/24/24	Tue 7/30/24	36																						
38		35	Seeding/Eros Control	2 days	Wed 7/31/24	Thu 8/1/24	37																						

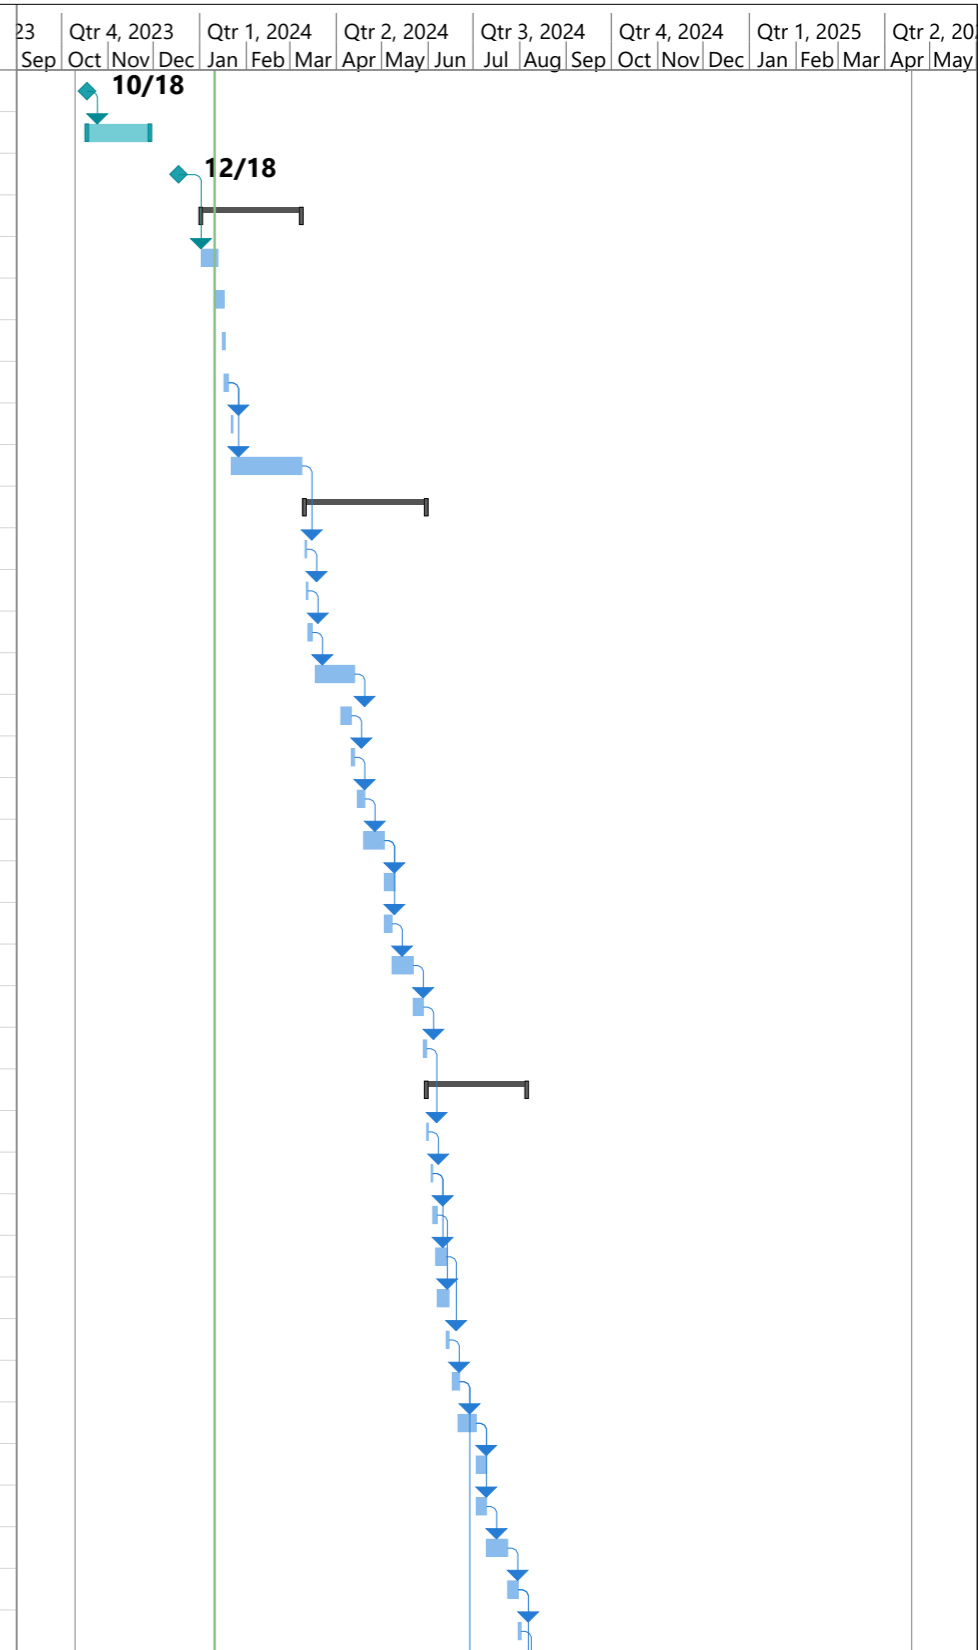

Project: KDOT SDG CO 0711 - S
Date: Thu 1/11/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Unique ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	23 Sep	Qtr 4, 2023	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025													
									Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	
39		36	Striping/Signing/Finishes	2 days	Fri 8/2/24	Mon 8/5/24	38																						
40		98	Stage 4 - Meridian {EAST 1/3}	67 days	Mon 6/24/24	Tue 9/24/24																							
41		99	Set Traffic Control {2WAY}	2 days	Mon 6/24/24	Tue 6/25/24	32																						
42		100	Rock Ex	3 days	Wed 6/26/24	Fri 6/28/24	41																						
43		101	Common Ex	5 days	Mon 7/1/24	Fri 7/5/24	42																						
44		102	Drainage Improvements	2 days	Mon 7/8/24	Tue 7/9/24	43																						
45		103	Finegrade	3 days	Mon 7/8/24	Wed 7/10/24	43																						
46		104	Crushed Rock Base	5 days	Thu 7/11/24	Wed 7/17/24	45																						
47		105	PCCP Mainline	30 days	Thu 8/1/24	Wed 9/11/24	46FS+10 days																						
48		106	C&G Slips/Handpours/Hookups	3 days	Thu 9/12/24	Mon 9/16/24	47																						
49		107	Drives & Valley Gutters {FORD ST}	3 days	Tue 9/17/24	Thu 9/19/24	48																						
50		108	Sidewalk, WCRs and Misc.	2 days	Fri 9/20/24	Mon 9/23/24	49																						
51		109	Seeding/Eros Control	1 day	Tue 9/24/24	Tue 9/24/24	50																						
52		37	Stage 3 - RR Header	29 days	Wed 7/31/24	Mon 9/9/24																							
53		38	Set Traffic Control {DETOUR}	2 days	Wed 7/31/24	Thu 8/1/24	37																						
54		39	Rock Exc	2 days	Fri 8/2/24	Mon 8/5/24	53																						
55		40	Common Ex	2 days	Tue 8/6/24	Wed 8/7/24	54																						
56		41	Crushed Rock Base	2 days	Thu 8/8/24	Fri 8/9/24	55																						
57		42	Finegrade	2 days	Mon 8/12/24	Tue 8/13/24	56																						
58		43	PCCP Pavement	10 days	Wed 8/14/24	Tue 8/27/24	57																						
59		44	C&G Slips/Handpours/Hookups	3 days	Wed 8/28/24	Fri 8/30/24	58																						
60		113	Cure time	5 days	Mon 9/2/24	Fri 9/6/24	59																						
61		45	Open To Traffic	1 day	Mon 9/9/24	Mon 9/9/24	60																						
62		61	Stage 5 - Meridian {WEST 1/3}	72 days	Wed 9/25/24	Thu 1/2/25																							
63		62	Set Traffic Control {2WAY}	2 days	Wed 9/25/24	Thu 9/26/24	51																						
64		63	Rock Ex	3 days	Fri 9/27/24	Tue 10/1/24	63																						
65		64	Common Ex	5 days	Wed 10/2/24	Tue 10/8/24	64																						
66		65	Drainage Imprvmnt & WATERLINE {INDUSTRIAL}	5 days	Wed 10/9/24	Tue 10/15/24	65																						
67		66	Finegrade	3 days	Wed 10/16/24	Fri 10/18/24	66																						
68		67	Crushed Rock Base	5 days	Mon 10/21/24	Fri 10/25/24	67																						
69		68	PCCP Mainline	10 days	Mon 10/28/24	Fri 11/8/24	68																						
70		69	C&G Slips/Handpours/Hookups	3 days	Mon 11/11/24	Wed 11/13/24	69																						
71		70	Drives & Valley Gutters	22 days	Thu 11/14/24	Fri 12/13/24	70																						
72		71	Sidewalk, WCRs and Misc.	10 days	Mon 12/16/24	Fri 12/27/24	71																						
73		72	Seeding/Eros Control	4 days	Mon 12/30/24	Thu 1/2/25	72																						
74		74	Stage 6 - Meridian {Centerlanes}	30 days	Thu 1/2/25	Wed 2/12/25																							
75		75	Set Traffic Control {2WAY}	2 days	Thu 1/2/25	Fri 1/3/25																							
76		76	Rock Ex	5 days	Mon 1/6/25	Fri 1/10/25	75																						

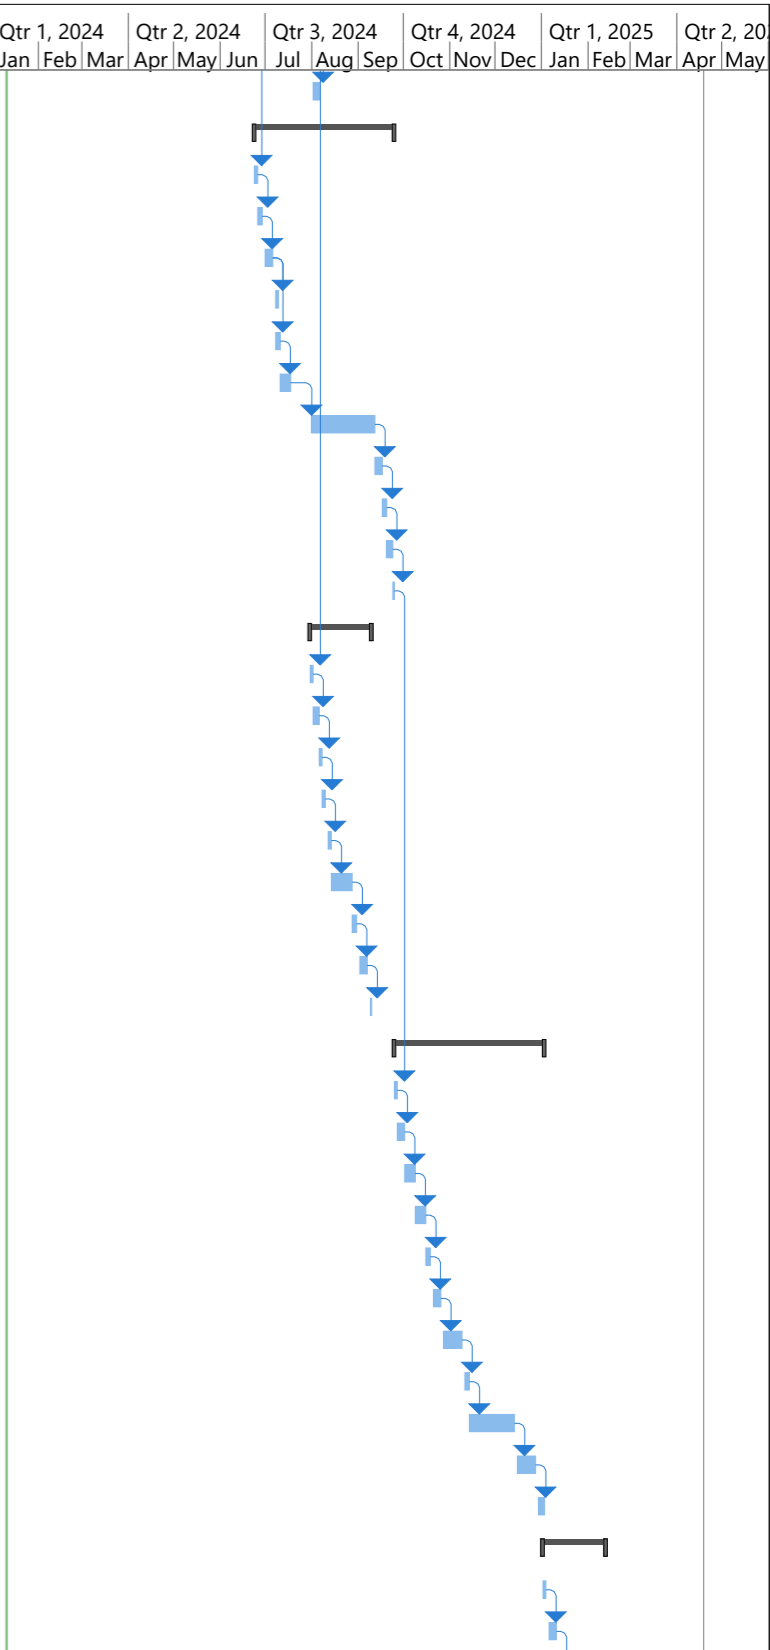

Project: KDOT SDG CO 0711 - S
Date: Thu 1/11/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

